

# Toffee Project Plan Details

Dr Alan M. McIvor

1 April 2000

## Abstract

The toffee report

## 1 Schedule

### 1.1 Time Frame

Start Date: 1999-03-09

Finish Date: 1999-11-30

### 1.2 Task list

- 5.2 Take notes  
*1999-07-20 - 1999-08-02; assigned to Albert E*  
Baseline  
*1999-03-16 - 1999-03-29*  
*Establish truth of reactions*
- 1.1 Specification  
*1999-03-09 - 1999-03-23; assigned to Alan McIvor*  
Baseline  
*1999-03-09 - 1999-03-22*  
*Develop operation specification*
- 1.2 Environment  
*1999-03-24 - 1999-03-26; assigned to Alan McIvor*  
Baseline  
*1999-03-09 - 1999-04-30*  
*Choose development environment*
- 1.3 Colour choice  
*1999-03-29 - 1999-03-31; assigned to Alan McIvor*  
Baseline  
*1999-03-23 - 1999-05-05*  
*Choose colours for toffee*

- 3.1 System Design  
*1999-04-01 - 1999-04-28; assigned to Alan McIvor*  
 Baseline  
*1999-04-28 - 1999-05-19*  
*Overall System Design*  

*2.1 changed from 10 to 6 days, based on completion of 100% in 6 days.*
- 2.1 GUI Design  
*1999-04-30 - 1999-06-25; assigned to Alan McIvor*  
 Baseline  
*1999-03-09 - 1999-03-29*  
*GUI Design*  

*2.1 changed from 10 to 6 days, based on completion of 100% in 6 days.*
- 3.2 Smell Implementationn  
*1999-05-03 - 1999-05-25; assigned to Alan McIvor*  
*Implement the smell that we want*  

*3.2 changed from 16 to 13 days, based on completion of 100% in 13 days.*
- 2.1b GUI Implementation  
*1999-06-28 - 1999-10-26; assigned to Alan McIvor*  
 Baseline  
*1999-03-30 - 1999-04-14*  
*Make the mess*  

*2.1b changed from 25 to 31 days, based on completion of 100% in 31 days.*
- 4.1 Colour refinement  
*1999-07-05 - 1999-08-27; assigned to Alan McIvor*  
 Baseline  
*1999-07-12 - 1999-08-13*  
*In-lab testing and tasting*  

*4.1 changed from 8 to 20 days, based on completion of 100% in 20 days.*
- 2.2 User Manual  
*1999-07-26 - 1999-09-24; assigned to Alan McIvor*  
 Baseline  
*1999-03-09 - 1999-04-29*  
*Get the manual GUI*  

*2.2 changed from 13 to 15 days, based on completion of 100% in 15 days.*

- 7.1 Virtual Toffee  
*1999-10-11 - 1999-11-12; assigned to Alan McIvor*  
 Baseline  
*1999-08-25 - 1999-08-25*  
*Virtual toffee implementation*
- 7.2 Set-up code  
*1999-10-27 - 1999-11-15; assigned to Alan McIvor*  
 Baseline  
*1999-09-14 - 1999-09-14*  
*Set-up code for virtual toffee*  

*7.2 changed from 7 to 4 days, based on completion of 100% in 4 days.*
- 8.2 Documentation  
*1999-11-22 - 1999-11-25; assigned to Alan McIvor*  
 Baseline  
*1999-09-10 - 1999-09-13*  
*Documentation*
- 5.1 Reaction Acquisition  
*1999-05-24 - 1999-07-19; assigned to Bacon Lettuce Tomato*  
 Baseline  
*1999-03-09 - 1999-03-15*  
*Acquire some reactions*
- 3.2b Smell Implementationn  
*1999-05-03 - 1999-06-10; assigned to John Simon*  
 Baseline  
*1999-05-20 - 1999-06-17*  
*Implement the smell that we want*  

*3.2b changed from 10 to 25 days, based on completion of 100% in 25 days.*
- 4.1b Colour refinement  
*1999-06-28 - 1999-08-26; assigned to John Simon*  
 Baseline  
*1999-07-12 - 1999-08-06*  
*In-lab testing and tasting*
- 8.2b Documentation  
*1999-08-27 - 1999-08-27; assigned to John Simon*  
 Baseline  
*1999-09-10 - 1999-09-13*

*Documentation*

*8.2b changed from 5 to 1 days, based on completion of 100% in 1 day.*

- 6.1 Evaluation  
*1999-10-15 - 1999-10-15; assigned to John Simon*  
Baseline  
*1999-08-25 - 1999-08-27*  
*Evaluation of feasibility*

- 3.2c Smell Implementationn  
*1999-04-06 - 1999-05-28; assigned to Laurie Daily*  
Baseline  
*1999-05-20 - 1999-07-08*  
*Implement the smell that we want*

*3.2c changed from 35 to 50 days, based on completion of 100% in 50 days.*

- 4.1c Colour refinement  
*1999-06-28 - 1999-09-17; assigned to Laurie Daily*  
Baseline  
*1999-07-12 - 1999-07-21*  
*In-lab testing and tasting*

*4.1c changed from 20 to 44 days, based on completion of 100% in 44 days.*

- 4.2 Field Trials  
*1999-09-20 - 1999-09-24; assigned to Laurie Daily*  
Baseline  
*1999-08-16 - 1999-08-20*  
*Field Trials*

- 7.1b Virtual toffee  
*1999-10-08 - 1999-11-01; assigned to Laurie Daily*  
Baseline  
*1999-08-25 - 1999-08-26*  
*Virtual toffee implementation*

- 6.1b Evaluation  
*1999-10-26 - 1999-10-26; assigned to Laurie Daily*  
Baseline  
*1999-08-25 - 1999-09-08*  
*Evaluation of feasibility*

- 8.2c Documentation  
*1999-11-02 - 1999-11-02; assigned to Laurie Daily*  
Baseline  
*1999-09-10 - 1999-09-20*  
Documentation  

*8.2c changed from 6 to 1 days, based on completion of 100% in 1 day.*
- 7.2b Set-up code  
*1999-11-15 - 1999-11-26; assigned to Laurie Daily*  
Baseline  
*1999-09-14 - 1999-09-15*  
*Set-up code for virtual toffee*
- 7.3 Field Trials  
*1999-11-29 - 1999-11-30; assigned to Laurie Daily*  
Baseline  
*1999-09-01 - 1999-09-07*  
*Field trials for virtual toffee*
- 1.1d Specification  
*1999-03-09 - 1999-03-11; assigned to Margaret Fleck*  
Baseline  
*1999-03-09 - 1999-03-09*  
*Develop operation specification*
- 1.3d Colour choice  
*1999-03-29 - 1999-03-31; assigned to Margaret Fleck*  
Baseline  
*1999-03-23 - 1999-03-23*  
*Choose colours for toffee*
- 3.1d System Design  
*1999-04-13 - 1999-04-26; assigned to Margaret Fleck*  
Baseline  
*1999-05-07 - 1999-05-07*  
*Overall System Design*  

*3.1d changed from 3 to 4 days, based on completion of 100% in 4 days.*
- 3.2d Smell Implementation  
*1999-05-10 - 1999-05-26; assigned to Margaret Fleck*  
Baseline  
*1999-05-20 - 1999-06-10*  

*3.2d changed from 12 to 18 days, based on completion of 100% in 18 days.*

- 4.2b Field Trials  
*1999-09-20 - 1999-10-14; assigned to Margaret Fleck*  
Baseline  
*1999-08-16 - 1999-08-23*  
*Yum Yum!!*
- 6.1c Evaluation  
*1999-10-15 - 1999-10-19; assigned to Suzzy Price*  
Baseline  
*1999-08-25 - 1999-08-27*  
*Evaluation of feasibility*

### 1.3 Milestone List

- 1 Preliminary Phase  
*1999-03-31*
- 3 Smell Implementationn  
*1999-06-10*
- 5 Trials  
*1999-08-02*
- 4 Colour Refinement  
*1999-10-14*
- 2 GUI Tools  
*1999-10-26*
- 6 Evaluation  
*1999-10-26*
- 8 Miscellaneous  
*1999-11-25*
- 7 Virtual toffee  
*1999-11-30*

### 1.4 Resources And Task Assignment

#### 1.4.1 Alan McIvor

Start	Finish	Days	Done	Task
1999-03-09	1999-03-23	11	11	1.1 Specification
1999-03-24	1999-03-26	3	3	1.2 Environment
1999-03-29	1999-03-31	3	3	1.3 Colour choise

1999-04-01	1999-04-28	13	13	3.1 System Design
1999-04-30	1999-06-25	6	6	2.1 GUI Design
1999-05-03	1999-05-25	13	13	3.2 Smell Implementationn
1999-06-28	1999-10-26	26	31	2.1b GUI Implementation
1999-07-05	1999-08-27	20	20	4.1 Colour refinement
1999-07-26	1999-09-24	15	15	2.2 User Manual
1999-10-11	1999-11-12	10	10	7.1 Virtual Toffee
1999-10-27	1999-11-15	4	4	7.2 Set-up code
1999-11-22	1999-11-25	4	4	8.2 Documentation

**Total: 128 days scheduled, 133 days completed.**

#### 1.4.2 John Simon

Start	Finish	Days	Done	Task
1999-05-03	1999-06-10	25	25	3.2b Smell Implementationn
1999-06-28	1999-08-26	25	25	4.1b Colour refinement
1999-08-27	1999-08-27	1	1	8.2b Documentation
1999-10-15	1999-10-15	1	0	6.1 Evaluation

**Total: 52 days scheduled, 51 days completed.**

#### 1.4.3 Laurie Daily

Start	Finish	Days	Done	Task
1999-04-06	1999-05-28	36	50	3.2c Smell Implementationn
1999-06-28	1999-09-17	44	44	4.1c Colour refinement
1999-09-20	1999-09-24	5	0	4.2 Field Trials
1999-10-08	1999-11-01	12	12	7.1b Virtual toffee
1999-10-26	1999-10-26	1	0	6.1b Evaluation
1999-11-02	1999-11-02	1	1	8.2c Documentation
1999-11-15	1999-11-26	6	6	7.2b Set-up code
1999-11-29	1999-11-30	2	0	7.3 Field Trials

**Total: 107 days scheduled, 113 days completed.**

#### 1.4.4 Gary Knight

Start	Finish	Days	Done	Task
-------	--------	------	------	------

**Total: 0 days scheduled, 0 days completed.**

#### 1.4.5 Bacon Lettuce Tomato

Start	Finish	Days	Done	Task
1999-05-24	1999-07-19	5	1	5.1 Reaction Acquisition

**Total: 5 days scheduled, 1 days completed.**

#### 1.4.6 Suzzy Price

Start	Finish	Days	Done	Task
1999-10-15	1999-10-19	3	0	6.1c Evaluation

**Total: 3 days scheduled, 0 days completed.**

#### 1.4.7 Albert E

Start	Finish	Days	Done	Task
1999-07-20	1999-08-02	10	1	5.2 Take notes

**Total: 10 days scheduled, 1 days completed.**

#### 1.4.8 Margaret Fleck

Start	Finish	Days	Done	Task
1999-03-09	1999-03-11	3	3	1.1d Specification
1999-03-29	1999-03-31	3	3	1.3d Colour choise
1999-04-13	1999-04-26	4	4	3.1d System Design
1999-05-10	1999-05-26	13	18	3.2d Smell Implementationn
1999-09-20	1999-10-14	19	19	4.2b Field Trials

**Total: 42 days scheduled, 47 days completed.**

### 1.5 Dependencies

- (1999-07-20 – 1999-08-02) Take notes
  - (1999-05-24 – 1999-07-19) Reaction Acquisition
- (1999-03-24 – 1999-03-26) Environment
  - (1999-03-09 – 1999-03-23) Specification
  - (1999-03-09 – 1999-03-11) Specification
- (1999-03-29 – 1999-03-31) Colour choise
  - (1999-03-24 – 1999-03-26) Environment
- (1999-04-01 – 1999-04-28) System Design
  - (1999-03-29 – 1999-03-31) Colour choise
  - (1999-03-29 – 1999-03-31) Colour choise
- (1999-04-30 – 1999-06-25) GUI Design
  - (1999-04-01 – 1999-04-28) System Design
- (1999-05-03 – 1999-05-25) Smell Implementationn
  - (1999-04-01 – 1999-04-28) System Design
  - (1999-04-13 – 1999-04-26) System Design
- (1999-06-28 – 1999-10-26) GUI Implementation

- (1999-04-30 – 1999-06-25) GUI Design
- (1999-07-05 – 1999-08-27) Colour refinement
  - (1999-05-03 – 1999-05-25) Smell Implementationn
  - (1999-05-03 – 1999-06-10) Smell Implementationn
  - (1999-04-06 – 1999-05-28) Smell Implementationn
  - (1999-05-10 – 1999-05-26) Smell Implementationn
- (1999-07-26 – 1999-09-24) User Manual
  - (1999-06-28 – 1999-10-26) GUI Implementation
- (1999-10-11 – 1999-11-12) Virtual Toffee
  - (1999-09-20 – 1999-09-24) Field Trials
  - (1999-09-20 – 1999-10-14) Field Trials
- (1999-10-27 – 1999-11-15) Set-up code
  - (1999-10-11 – 1999-11-12) Virtual Toffee
  - (1999-10-08 – 1999-11-01) Virtual toffee
- (1999-11-22 – 1999-11-25) Documentation
  - (1999-10-15 – 1999-10-15) Evaluation
  - (1999-10-26 – 1999-10-26) Evaluation
  - (1999-10-15 – 1999-10-19) Evaluation
  - (1999-11-29 – 1999-11-30) Field Trials
- (1999-05-24 – 1999-07-19) Reaction Acquisition
  - (1999-04-01 – 1999-04-28) System Design
- (1999-05-03 – 1999-06-10) Smell Implementationn
  - (1999-04-01 – 1999-04-28) System Design
  - (1999-04-13 – 1999-04-26) System Design
- (1999-06-28 – 1999-08-26) Colour refinement
  - (1999-05-03 – 1999-05-25) Smell Implementationn
  - (1999-05-03 – 1999-06-10) Smell Implementationn
  - (1999-04-06 – 1999-05-28) Smell Implementationn
  - (1999-05-10 – 1999-05-26) Smell Implementationn
- (1999-08-27 – 1999-08-27) Documentation

- (1999-10-15 – 1999-10-15) Evaluation
- (1999-10-26 – 1999-10-26) Evaluation
- (1999-10-15 – 1999-10-19) Evaluation
- (1999-11-29 – 1999-11-30) Field Trials
- (1999-10-15 – 1999-10-15) Evaluation
  - (1999-09-20 – 1999-09-24) Field Trials
  - (1999-09-20 – 1999-10-14) Field Trials
- (1999-04-06 – 1999-05-28) Smell Implementationn
  - (1999-04-01 – 1999-04-28) System Design
  - (1999-04-13 – 1999-04-26) System Design
- (1999-06-28 – 1999-09-17) Colour refinement
  - (1999-05-03 – 1999-05-25) Smell Implementationn
  - (1999-05-03 – 1999-06-10) Smell Implementationn
  - (1999-04-06 – 1999-05-28) Smell Implementationn
  - (1999-05-10 – 1999-05-26) Smell Implementationn
- (1999-09-20 – 1999-09-24) Field Trials
  - (1999-07-05 – 1999-08-27) Colour refinement
  - (1999-06-28 – 1999-08-26) Colour refinement
  - (1999-06-28 – 1999-09-17) Colour refinement
- (1999-10-08 – 1999-11-01) Virtual toffee
  - (1999-09-20 – 1999-09-24) Field Trials
  - (1999-09-20 – 1999-10-14) Field Trials
- (1999-10-26 – 1999-10-26) Evaluation
  - (1999-09-20 – 1999-09-24) Field Trials
  - (1999-09-20 – 1999-10-14) Field Trials
- (1999-11-02 – 1999-11-02) Documentation
  - (1999-10-15 – 1999-10-15) Evaluation
  - (1999-10-26 – 1999-10-26) Evaluation
  - (1999-10-15 – 1999-10-19) Evaluation
  - (1999-11-29 – 1999-11-30) Field Trials
- (1999-11-15 – 1999-11-26) Set-up code

- (1999-10-11 – 1999-11-12) Virtual Toffee
- (1999-10-08 – 1999-11-01) Virtual toffee
- (1999-11-29 – 1999-11-30) Field Trials
  - (1999-10-27 – 1999-11-15) Set-up code
  - (1999-11-15 – 1999-11-26) Set-up code
- (1999-03-29 – 1999-03-31) Colour choise
  - (1999-03-24 – 1999-03-26) Environment
- (1999-04-13 – 1999-04-26) System Design
  - (1999-03-29 – 1999-03-31) Colour choise
  - (1999-03-29 – 1999-03-31) Colour choise
- (1999-05-10 – 1999-05-26) Smell Implementationn
  - (1999-04-01 – 1999-04-28) System Design
  - (1999-04-13 – 1999-04-26) System Design
- (1999-09-20 – 1999-10-14) Field Trials
  - (1999-07-05 – 1999-08-27) Colour refinement
  - (1999-06-28 – 1999-08-26) Colour refinement
  - (1999-06-28 – 1999-09-17) Colour refinement
- (1999-10-15 – 1999-10-19) Evaluation
  - (1999-09-20 – 1999-09-24) Field Trials
  - (1999-09-20 – 1999-10-14) Field Trials

## 1.6 Vacations

### 1.6.1 Alan McIvor

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-04-12	1999-04-16	5
1999-06-07	1999-06-07	1
1999-08-30	1999-08-31	2
1999-09-27	1999-10-08	10
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4
1999-11-29	1999-12-03	5

### 1.6.2 John Simon

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-06-07	1999-06-07	1
1999-08-02	1999-08-06	5
1999-08-30	1999-08-31	2
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

### 1.6.3 Laurie Daily

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-04-30	1999-04-30	1
1999-06-07	1999-06-07	1
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

### 1.6.4 Gary Knight

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-06-07	1999-06-07	1
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

### 1.6.5 Bacon Lettuce Tomato

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-04-07	1999-04-07	1
1999-04-14	1999-04-14	1
1999-04-21	1999-04-21	1
1999-04-28	1999-04-28	1
1999-05-05	1999-05-05	1
1999-05-12	1999-05-12	1
1999-05-19	1999-05-19	1
1999-05-25	1999-06-04	9
1999-06-07	1999-06-07	1
1999-06-08	1999-07-12	25
1999-07-14	1999-07-14	1

1999-07-21	1999-07-21	1
1999-07-28	1999-07-28	1
1999-08-04	1999-08-04	1
1999-08-11	1999-08-11	1
1999-08-18	1999-08-18	1
1999-08-25	1999-08-25	1
1999-09-01	1999-09-01	1
1999-09-08	1999-09-08	1
1999-09-15	1999-09-15	1
1999-09-22	1999-09-22	1
1999-09-29	1999-09-29	1
1999-10-06	1999-10-06	1
1999-10-13	1999-10-13	1
1999-10-20	1999-10-20	1
1999-10-25	1999-10-25	1
1999-10-27	1999-10-27	1
1999-11-16	1999-11-19	4

#### 1.6.6 Suzzy Price

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-06-07	1999-06-07	1
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

#### 1.6.7 Albert E

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-06-07	1999-06-07	1
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

#### 1.6.8 Margaret Fleck

Start	Finish	Days
1999-04-02	1999-04-05	2
1999-06-07	1999-06-07	1
1999-10-25	1999-10-25	1
1999-11-16	1999-11-19	4

## 2 Weekly tasks

## **2.1 Week of 1999-03-09**

- **Alan McIvor**
  - 4 days - 1.1 - Specification.  
(11 days completed.)
- **Margaret Fleck**
  - 3 days - 1.1d - Specification.  
(3 days completed.)

## **2.2 Week of 1999-03-15**

- **Alan McIvor**
  - 5 days - 1.1 - Specification.  
(11 days completed.)

## **2.3 Week of 1999-03-22**

- **Alan McIvor**
  - 2 days - 1.1 - Specification.  
(11 days completed.)
  - 3 days - 1.2 - Environment.  
(3 days completed.)

## **2.4 Week of 1999-03-29**

- **Alan McIvor**

- 3 days - 1.3 - Colour choice.  
(3 days completed.)
- 1 days - 3.1 - System Design.  
(13 days completed.)

- **Margaret Fleck**

- 3 days - 1.3d - Colour choice.  
(3 days completed.)

## **2.5 Week of 1999-04-05**

- **Alan McIvor**

- 4 days - 3.1 - System Design.  
(13 days completed.)

- **Laurie Daily**

- 4 days - 3.2c - Smell Implementationn.  
(50 days completed.)

## **2.6 Week of 1999-04-12**

- **Laurie Daily**

- 5 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 1 days - 3.1d - System Design.  
(4 days completed.)

## **2.7 Week of 1999-04-19**

- **Alan McIvor**

- 5 days - 3.1 - System Design.  
(13 days completed.)

- **Laurie Daily**

- 5 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 2 days - 3.1d - System Design.  
(4 days completed.)

## 2.8 Week of 1999-04-26

- **Alan McIvor**

- 1 days - 2.1 - GUI Design.  
(6 days completed.)
- 3 days - 3.1 - System Design.  
(13 days completed.)

- **Laurie Daily**

- 4 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 1 days - 3.1d - System Design.  
(4 days completed.)

## **2.9 Week of 1999-05-03**

- **Alan McIvor**

- 5 days - 3.2 - Smell Implementationn.  
(13 days completed.)

- **John Simon**

- 5 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 3 days - 3.2c - Smell Implementationn.  
(50 days completed.)

## 2.10 Week of 1999-05-10

- **Alan McIvor**

- 5 days - 3.2 - Smell Implementationn.  
(13 days completed.)

- **John Simon**

- 5 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 5 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 5 days - 3.2d - Smell Implementationn.  
(18 days completed.)

## **2.11 Week of 1999-05-17**

- **Alan McIvor**

- 2 days - 3.2 - Smell Implementationn.  
(13 days completed.)

- **John Simon**

- 5 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 5 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 5 days - 3.2d - Smell Implementationn.  
(18 days completed.)

## 2.12 Week of 1999-05-24

- **Alan McIvor**

- 1 days - 3.2 - Smell Implementationn.  
(13 days completed.)
- Paused: 3.2 - Smell Implementationn.

- **John Simon**

- 5 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 5 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Bacon Lettuce Tomato**

- 1 days - 5.1 - Reaction Acquisition.  
(1 days completed.)

- **Margaret Fleck**

- 3 days - 3.2d - Smell Implementationn.  
(18 days completed.)

## **2.13 Week of 1999-05-31**

- **John Simon**

- 2 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 1 days - 3.2c - Smell Implementationn.  
(50 days completed.)
- 4 days - 3.2c - Smell Implementationn.  
(50 days completed.)

## **2.14 Week of 1999-06-07**

- **John Simon**

- 3 days - 3.2b - Smell Implementationn.  
(25 days completed.)

- **Laurie Daily**

- 3 days - 3.2c - Smell Implementationn.  
(50 days completed.)

## **2.15 Week of 1999-06-14**

- **Laurie Daily**

- 4 days - 3.2c - Smell Implementationn.  
(50 days completed.)

- **Margaret Fleck**

- 5 days - 3.2d - Smell Implementationn.  
(18 days completed.)

## **2.16 Week of 1999-06-21**

- **Alan McIvor**

- 5 days - 2.1 - GUI Design.  
(6 days completed.)

- **Laurie Daily**

- 2 days - 3.2c - Smell Implementationn.  
(50 days completed.)

## **2.17 Week of 1999-06-28**

- **Alan McIvor**
  - 5 days - 2.1b - GUI Implementation.  
(31 days completed.)
- **John Simon**
  - 5 days - 4.1b - Colour refinement.  
(25 days completed.)
- **Laurie Daily**
  - 4 days - 4.1c - Colour refinement.  
(44 days completed.)

## **2.18 Week of 1999-07-05**

- **Alan McIvor**
  - 5 days - 4.1 - Colour refinement.  
(20 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)

## 2.19 Week of 1999-07-12

- **John Simon**

- 5 days - 4.1b - Colour refinement.  
(25 days completed.)

- **Laurie Daily**

- 5 days - 4.1c - Colour refinement.  
(44 days completed.)

- **Bacon Lettuce Tomato**

- 1 days - 5.1 - Reaction Acquisition.  
(1 days completed.)
- 2 days - 5.1 - Reaction Acquisition.  
(1 days completed.)

## 2.20 Week of 1999-07-19

- **Alan McIvor**
  - 5 days - 2.1b - GUI Implementation.  
(31 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)
- **Bacon Lettuce Tomato**
  - 1 days - 5.1 - Reaction Acquisition.  
(1 days completed.)
- **Albert E**
  - 4 days - 5.2 - Take notes.  
(1 days completed.)

## **2.21 Week of 1999-07-26**

- **Alan McIvor**
  - 5 days - 2.2 - User Manual.  
(15 days completed.)
- **John Simon**
  - 1 days - 4.1b - Colour refinement.  
(25 days completed.)
- **Albert E**
  - 5 days - 5.2 - Take notes.  
(1 days completed.)

## **2.22 Week of 1999-08-02**

- **Alan McIvor**
  - 5 days - 2.1b - GUI Implementation.  
(31 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)
- **Albert E**
  - 1 days - 5.2 - Take notes.  
(1 days completed.)

## **2.23 Week of 1999-08-09**

- **Alan McIvor**
  - 5 days - 4.1 - Colour refinement.  
(20 days completed.)
- **John Simon**
  - 5 days - 4.1b - Colour refinement.  
(25 days completed.)

## **2.24 Week of 1999-08-16**

- **Alan McIvor**
  - 5 days - 4.1 - Colour refinement.  
(20 days completed.)
- **John Simon**
  - 5 days - 4.1b - Colour refinement.  
(25 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)

## **2.25 Week of 1999-08-23**

- **Alan McIvor**

- 5 days - 4.1 - Colour refinement.  
(20 days completed.)

- **John Simon**

- 4 days - 4.1b - Colour refinement.  
(25 days completed.)
- 1 days - 8.2b - Documentation.  
(1 days completed.)

- **Laurie Daily**

- 5 days - 4.1c - Colour refinement.  
(44 days completed.)

## **2.26 Week of 1999-08-30**

- Nothing in Week of 1999-08-30

## **2.27 Week of 1999-09-06**

- **Alan McIvor**
  - 5 days - 2.1b - GUI Implementation.  
(31 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)

## **2.28 Week of 1999-09-13**

- **Alan McIvor**
  - 5 days - 2.2 - User Manual.  
(15 days completed.)
- **Laurie Daily**
  - 5 days - 4.1c - Colour refinement.  
(44 days completed.)

## **2.29 Week of 1999-09-20**

- **Alan McIvor**
  - 5 days - 2.2 - User Manual.  
(15 days completed.)
- **Laurie Daily**
  - 5 days - 4.2 - Field Trials.
- **Margaret Fleck**
  - 5 days - 4.2b - Field Trials.  
(19 days completed.)

### **2.30 Week of 1999-09-27**

- **Margaret Fleck**
  - 5 days - 4.2b - Field Trials.  
(19 days completed.)

### **2.31 Week of 1999-10-04**

- **Laurie Daily**

- 1 days - 7.1b - Virtual toffee.  
(12 days completed.)

- **Margaret Fleck**

- 5 days - 4.2b - Field Trials.  
(19 days completed.)

### **2.32 Week of 1999-10-11**

- **Alan McIvor**
  - 5 days - 7.1 - Virtual Toffee.  
(10 days completed.)
- **John Simon**
  - 1 days - 6.1 - Evaluation.
- **Laurie Daily**
  - 5 days - 7.1b - Virtual toffee.  
(12 days completed.)
- **Suzzy Price**
  - 1 days - 6.1c - Evaluation.
- **Margaret Fleck**
  - 4 days - 4.2b - Field Trials.  
(19 days completed.)

### **2.33 Week of 1999-10-18**

- **Alan McIvor**
  - 5 days - 2.1b - GUI Implementation.  
(31 days completed.)
- **Laurie Daily**
  - 5 days - 7.1b - Virtual toffee.  
(12 days completed.)
- **Suzzy Price**
  - 2 days - 6.1c - Evaluation.

## **2.34 Week of 1999-10-25**

- **Alan McIvor**

- 1 days - 2.1b - GUI Implementation.  
(31 days completed.)
- 3 days - 7.2 - Set-up code.  
(4 days completed.)

- **Laurie Daily**

- 1 days - 6.1b - Evaluation.

## **2.35 Week of 1999-11-01**

- **Alan McIvor**

- 5 days - 2.1b - GUI Implementation.  
(31 days completed.)

- **Laurie Daily**

- 1 days - 7.1b - Virtual toffee.  
(12 days completed.)
- 1 days - 8.2c - Documentation.  
(1 days completed.)

## **2.36 Week of 1999-11-08**

- **Alan McIvor**

- 5 days - 7.1 - Virtual Toffee.  
(10 days completed.)

### **2.37 Week of 1999-11-15**

- **Alan McIvor**

- 1 days - 7.2 - Set-up code.  
(4 days completed.)

- **Laurie Daily**

- 1 days - 7.2b - Set-up code.  
(6 days completed.)

## **2.38 Week of 1999-11-22**


- **Alan McIvor**
  - 4 days - 8.2 - Documentation.  
(4 days completed.)
- **Laurie Daily**
  - 5 days - 7.2b - Set-up code.  
(6 days completed.)

### **2.39 Week of 1999-11-29**


- **Laurie Daily**


- 2 days - 7.3 - Field Trials.


3 Resource Utilisation




## 4 GANTT Charts

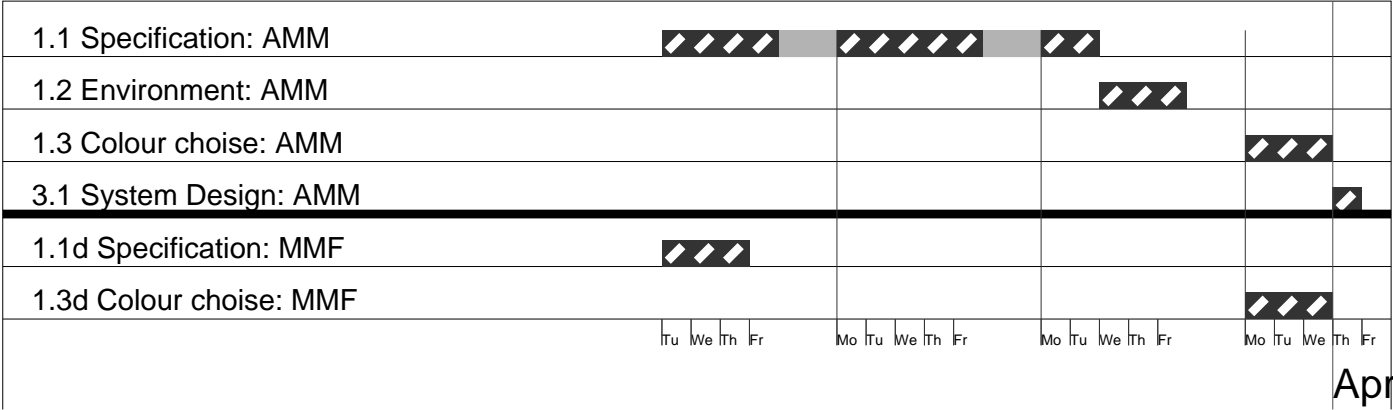

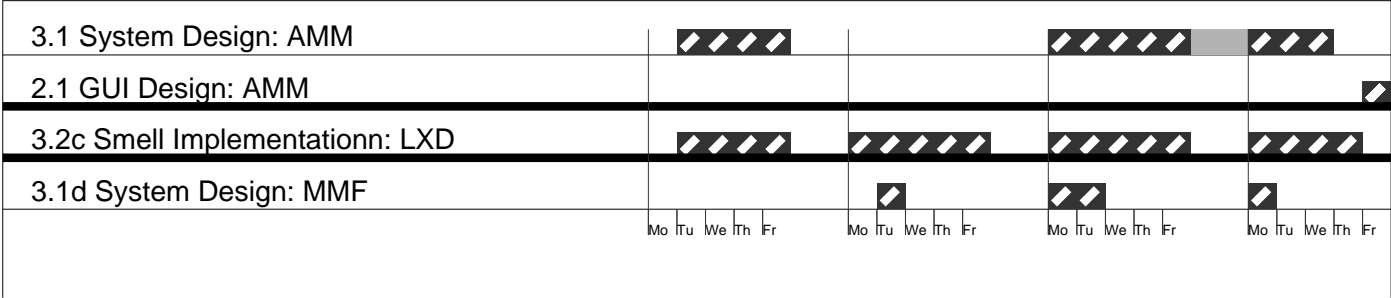

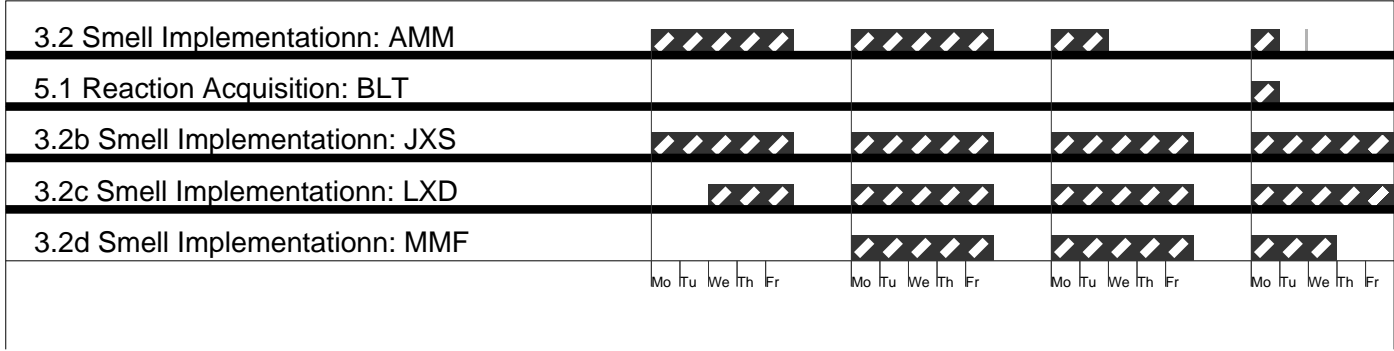

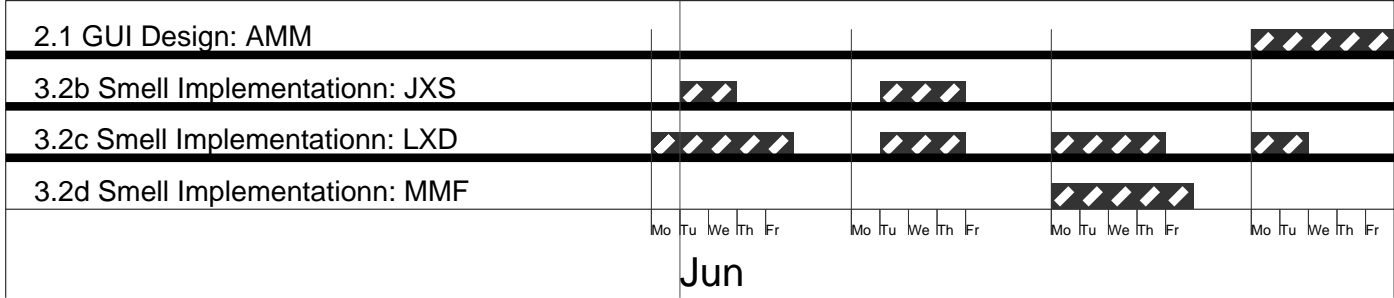

4.5 1999.Jun.28 1999.Jul.23

